

**OAN 069/2020 – STAND 211
LIFT SHAFT & SCAFFOLDING REMOVAL**

OAN REF:-	069/2020	DATE OF ISSUE:-	10/07/20	EFFECTIVE DATE:-	13/07/20
MANUAL REFERENCE(S):-	N A			EXPIRY DATE:-	26/09/20

PLEASE ENSURE THIS INFORMATION IS PROMULGATED TO ALL STAFF

1.0 SUMMARY

1.1 An eleven-week programme of works to carry out the removal of a temporary lift shaft and scaffolding from the head of Stand 211.

2.0 PROGRAMME

2.1 The overall programme of work will commence on Monday 13th July and be completed by Saturday 26th September 2020.

2.2 Daily working hours will be 07:30 – 18:00L, Monday to Friday.

2.3 Any weekend working required will be arranged directly with the Airfield Duty Manager (ADM).

3.0 SCOPE & LOCATION OF WORKS

3.1 All works will be located within a fenced works compound on Stand 211.

3.2 The overall scope of works will be as follows:

- Position skip at the head of stand 211 behind airbridge.
- Enclose the works area with water filled red and white blocks and lit Heras fencing with secure gated access.
- Full isolation of services to Busing Lounge.
- Removal of all services from scaffolding.
- Removal of tin roof sheeting, shrink wrap and scaffold.
- Cladding reinstatement.
- Removal by crane of lift shafts onto articulated wagons.
- Break out PQ slabs to install underground services.
- Reinstatement concrete.

4.0 OPERATIONAL IMPLICATIONS

- 4.1 For phase 1, a skip will be positioned at the head of Stand 211 behind the airbridge on Tuesday 14th July 2020 and the area will be fenced locally enabling the stand to still be used for aircraft turnround.
- 4.2 For phase 2, Stand 211 will be closed H24 from Monday 27th July 2020 for the duration of the works.
- 4.3 See attached drawing for skip location and fence location for each phase.

5.0 LOW VISIBILITY OPERATIONS (LVO)



- 5.1 The work has no effect on existing low visibility procedures.

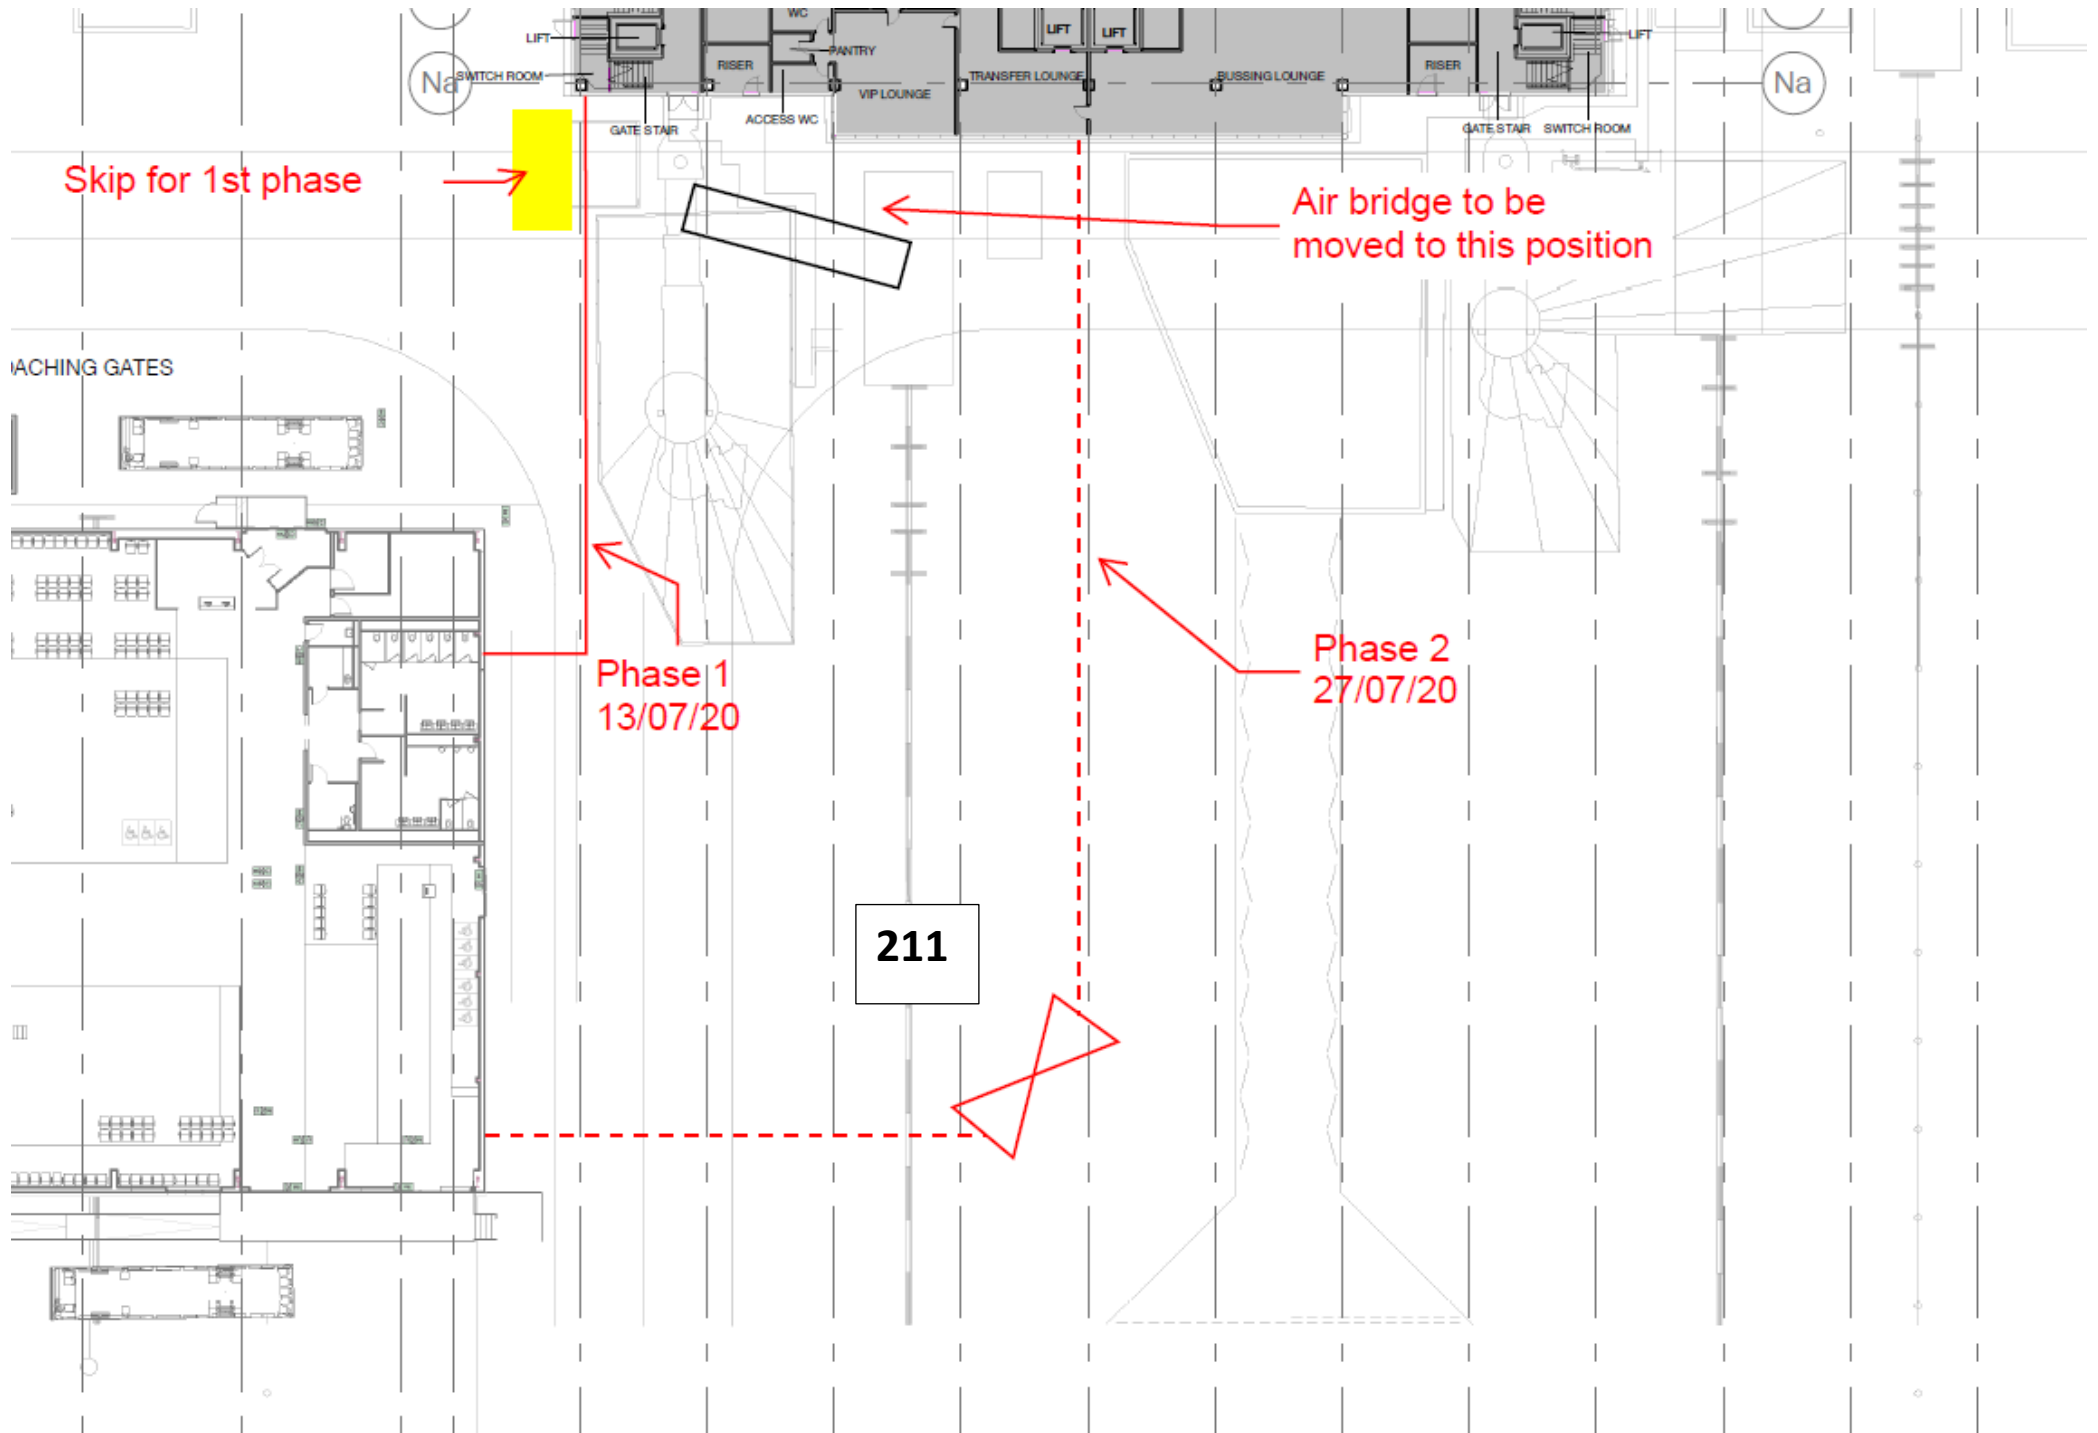
6.0 FURTHER INFORMATION

- 6.1 For further information, please contact the Airfield Duty Manager on +44 161 489 3331.

7.0 ADDITIONAL DOCUMENTS

- 7.1 Drawing: Yes Annexe: No

ORIGINATOR:-	E. YATES	CONFIRMED & APPROVED BY:-	C.Wild
ROLE:-	AIRFIELD TECHNICAL PLANNER	ROLE:-	Head of Airfield Operations
SIGNATURE:		SIGNATURE:-	



Skip for 1st phase

Air bridge to be moved to this position

Phase 1
13/07/20

Phase 2
27/07/20

211
