

OAN 073/2020 – REMOVAL OF TEMPORARY CRITICAL PART FENCE – TAXIWAY ZULU.

OAN REF:-	073/2020	DATE OF ISSUE:-	17/07/20	EFFECTIVE DATE:-	23/07/20
MANUAL REFERENCE(S):-	N/A			EXPIRY DATE:-	21/08/20

PLEASE ENSURE THIS INFORMATION IS PROMULGATED TO ALL STAFF

1.0 SUMMARY

1.1 A programme of up to four weeks work to remove the temporary Critical Part (CP) fence currently in-situ along the western edge of Taxiway Zulu.

2.0 PROGRAMME

2.1 The overall programme of work will commence on Thursday 23rd July and is scheduled to be completed by Friday 21st August 2020.

2.2 The work will take place Monday to Friday, the majority of which will be undertaken during daylight hours, nominally 07:00 – 17:00L.

2.3 Some minor elements of work will be undertaken at night (two nights' work) with nominal working hours of 22:00 – 06:00L.

3.0 SCOPE & LOCATION OF WORKS

3.1 All work will be located on Taxiway Zulu in the immediate vicinity of the temporary CP fence opposite Pier 1.

The overall scope of work will entail the following tasks;

- Removal of temporary CP fence, concrete barriers and melba logs (circa 50m per day).
- Transport of concrete blocks for storage at a designated airside area.
- Filling and over-coring of pavement bolt holes.
- Pavement joint sealing along the previous location of the temporary CP fence.

The attached drawing depicts the overall working location.

4.0 OPERATIONAL IMPLICATIONS

- 4.1 No specific operational implications are anticipated as a result of this work.
- 4.2 The works scope and methodology are such that the contractor will be able to temporarily vacate Taxiway Zulu in the event of an aircraft movement past the area of work in progress.

5.0 LOW VISIBILITY PROCEDURES

- 5.1 In the event of forecast low visibility, the planned work on Taxiway Zulu will be cancelled.


6.0 IMMEDIATE AIRFIELD CHANGES


- 6.1 The work described in this OAN is enabling work prior to the imminent opening of new airfield infrastructure, namely, new remote stands and a dual centreline system on Taxiway Zulu.
- 6.2 Specific operational information regarding the introduction of the new infrastructure into service will be promulgated via a separate OAN.

7.0 ADDITIONAL DOCUMENTS

Drawing: Yes

TAXIWAY ZULU TEMPORARY
CP FENCE REMOVAL.

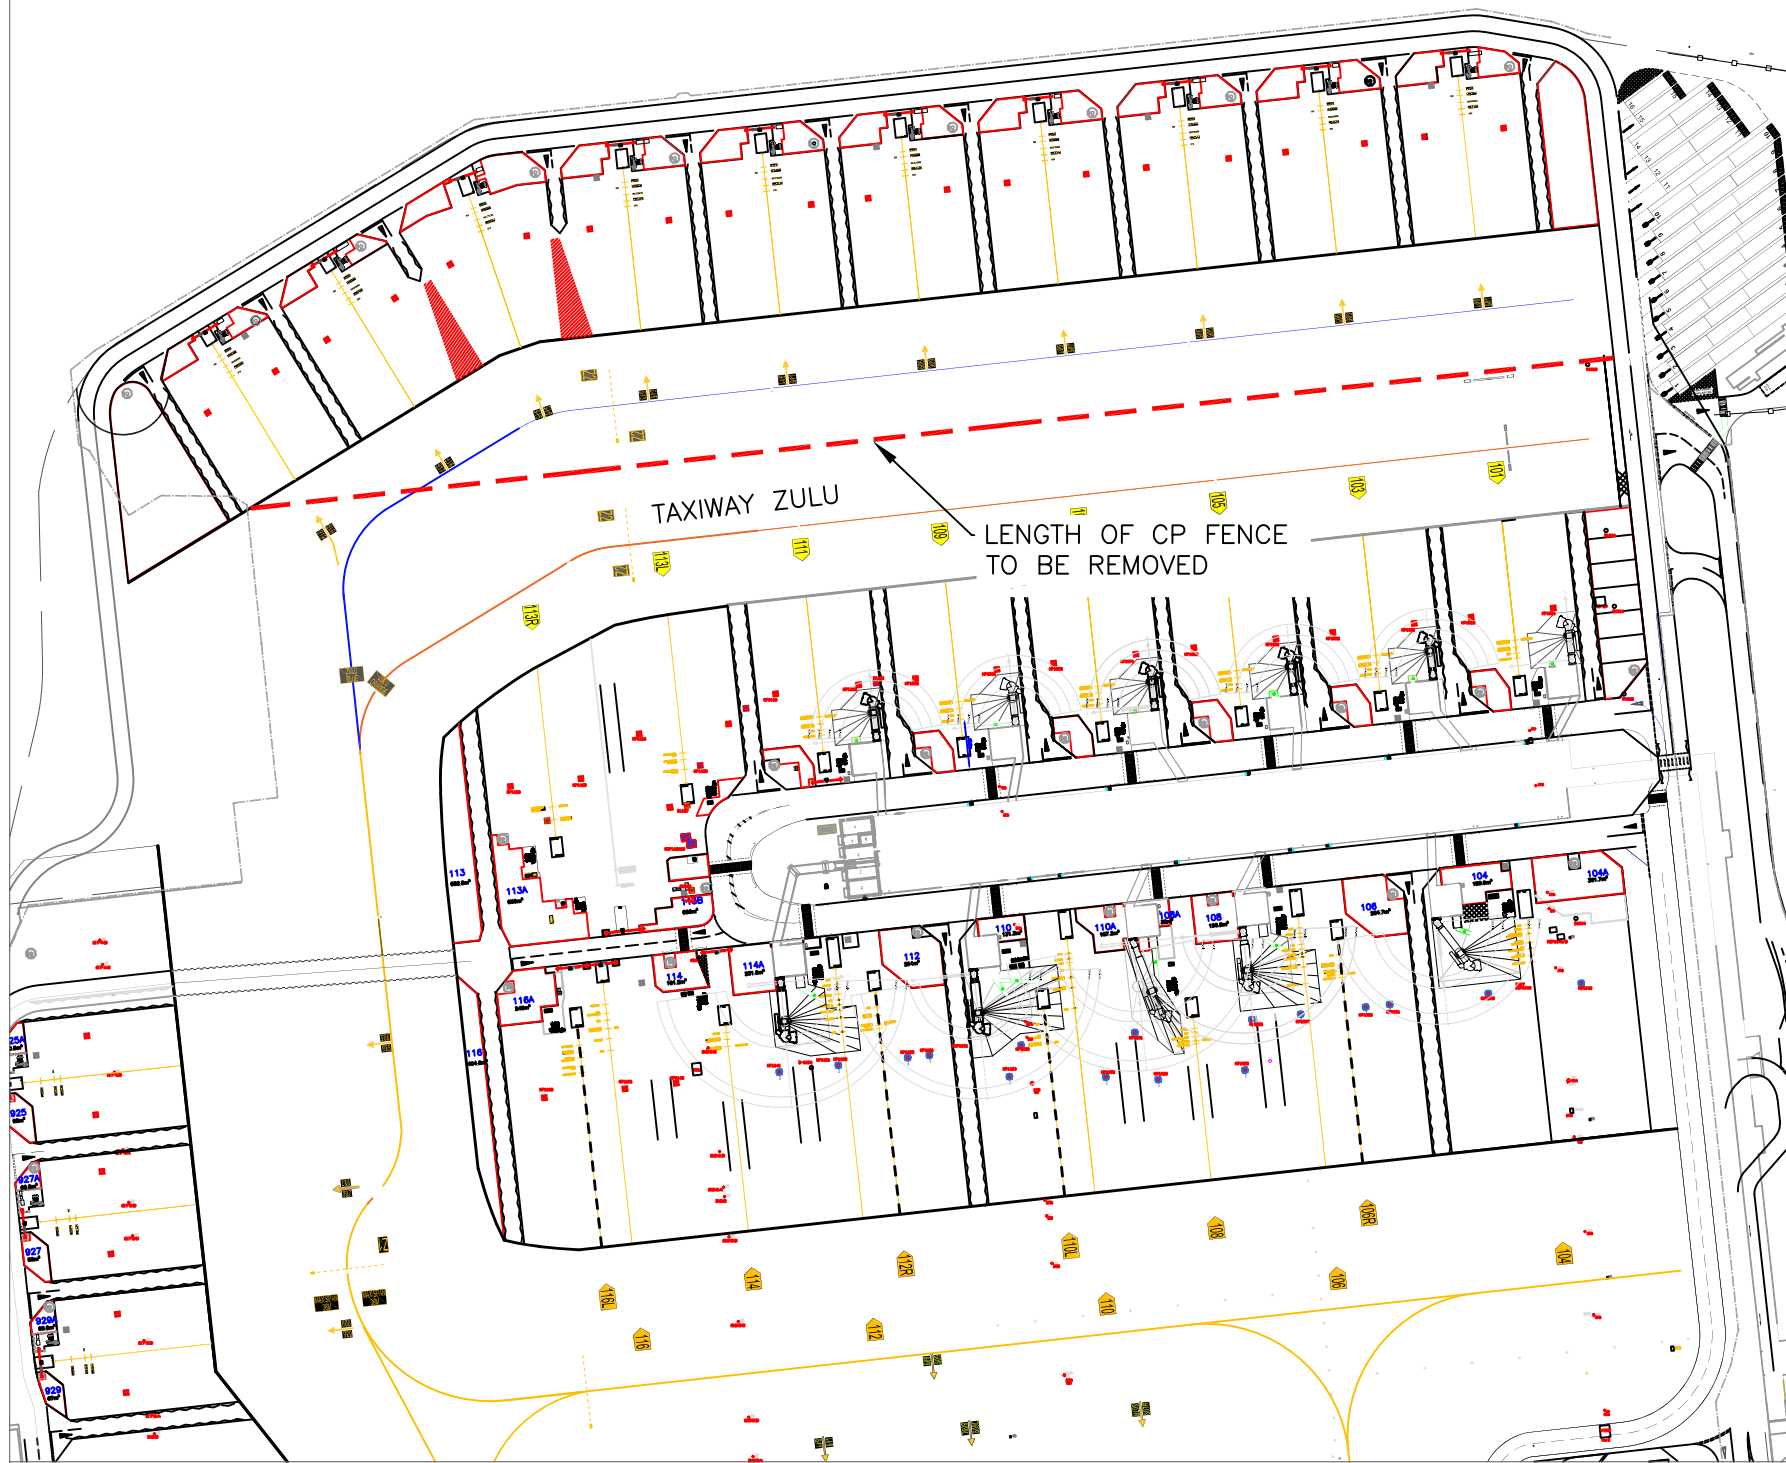

ORIGINATOR:-	S.MCALEER	CONFIRMED & APPROVED BY:-	C.WILD
ROLE:-	AIRFIELD TECHNICAL PLANNER	ROLE:-	HEAD OF AIRFIELD OPERATIONS
SIGNATURE:-		SIGNATURE:-	
